



ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	
1			CUMMINGS LOFT PROJECT	165 days	Fri 5/1/26	Thu 12/17/26			
2			GENERAL CONDITIONS	1 day	Fri 5/1/26	Fri 5/1/26			
3			Prepare and submit schedule of values	1 day	Fri 5/1/26	Fri 5/1/26		GC PM	
4			Submit bonds insurance documents	1 day	Fri 5/1/26	Fri 5/1/26		GC PM	
5			Prepare and submit project schedule	1 day	Fri 5/1/26	Fri 5/1/26		GC PM	
6			Sign contract	1 day	Fri 5/1/26	Fri 5/1/26		GC Management	
7			Schedule and conduct pre-construction meeting	1 day	Fri 5/1/26	Fri 5/1/26		Client PM	
8			MOBILIZATION	1 day	Fri 5/1/26	Fri 5/1/26			
9			Prepare site - install temporary facilities	1 day	Fri 5/1/26	Fri 5/1/26		GC Crew	
10			DEMOLITION	110 days	Mon 5/4/26	Fri 10/2/26			
11			Prepare site for demolition	1 day	Mon 5/4/26	Mon 5/4/26	9	GC Crew	
12			Demolish existing flooring	1 day	Tue 5/5/26	Tue 5/5/26	11	GC Crew	
13			Open exterior walls for new windows	2 days	Wed 5/6/26	Thu 5/7/26	12	GC Crew	
14			Demolish door	1 day	Tue 9/22/26	Tue 9/22/26	13	GC Crew	
15			Open wall for new door	3 days	Wed 9/30/26	Fri 10/2/26	13	GC Crew	
16			WOOD, PLASTIC AND COMPOSITES	5 days	Mon 9/14/26	Fri 9/18/26		GC Crew	
17			Install windows framing	5 days	Mon 9/14/26	Fri 9/18/26		GC Crew	
18			Install interior wall framing	5 days	Mon 9/14/26	Fri 9/18/26		GC Crew	
19			Install door framing	5 days	Mon 9/14/26	Fri 9/18/26		GC Crew	
20			OPENINGS	50 days	Mon 9/21/26	Fri 11/27/26			
21			Install 3 windows	50 days	Mon 9/21/26	Fri 11/27/26		GC Crew	
22			Install aluminum-glass storefront and doors	50 days	Mon 9/21/26	Fri 11/27/26		GC Crew	
23			ROUGH ELECTRICAL	30 days	Mon 9/21/26	Fri 10/30/26			

Project: Loft Project Schedule 6
Date: Fri 9/11/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	
24			Wire for duplex, quad, GFCI outlets	5 days	Mon 9/21/26	Fri 9/25/26		GC Crew	
25			Wire for new data outlets	5 days	Mon 9/21/26	Fri 9/25/26		GC Crew	
26			Wire for new 200 Amp panel, new meter	5 days	Mon 9/21/26	Fri 9/25/26		GC Crew	
27			Fire alarm integration	30 days	Mon 9/21/26	Fri 10/30/26		GC Crew	
28			ROUGH PLUMBING	10 days	Mon 9/14/26	Fri 9/25/26			
29			Install pipe works for water lines, vents and waste pipe	10 days	Mon 9/14/26	Fri 9/25/26		GC Crew	
30			ROUGH MECHANICAL	14 days	Mon 9/28/26	Thu 10/15/26			
31			Install HVAC system	14 days	Mon 9/28/26	Thu 10/15/26		GC Crew	
32			THERMAL AND FINISHES	18 days	Mon 9/28/26	Wed 10/21/26			
33			Install insulation	2 days	Mon 9/28/26	Tue 9/29/26		GC Crew	
34			Install gypsum board	5 days	Wed 9/30/26	Tue 10/6/26	33	GC Crew	
35			Wall patching and texturing	5 days	Wed 10/7/26	Tue 10/13/26	34	GC Crew	
36			Paint walls per finishes schedule	4 days	Wed 10/14/26	Mon 10/19/26	35	GC Crew	
37			Paint doors and trim	2 days	Tue 10/20/26	Wed 10/21/26	36	GC Crew	
38			FINE ELECTRICAL	24 days	Mon 9/21/26	Thu 10/22/26			
39			Install lighting fixtures per schedule	5 days	Fri 10/16/26	Thu 10/22/26	31	GC Crew	
40			Install duplex, quad, GFCI outlets	5 days	Mon 9/28/26	Fri 10/2/26	26	GC Crew	
41			Install new data outlets	2 days	Mon 9/28/26	Tue 9/29/26	26	GC Crew	
42			Install new 200 Amp panel, new meter	2 days	Mon 9/21/26	Tue 9/22/26		GC Crew	
43			FINISHES	20 days	Mon 11/16/26	Fri 12/11/26			
44			Install lower and upper kitchen cabinets	2 days	Mon 11/16/26	Tue 11/17/26		GC Crew	
45			Install granite countertops	1 day	Wed 11/18/26	Wed 11/18/26	44	GC Crew	
46			Install kitchen and restroom accessories	1 day	Thu 11/19/26	Thu 11/19/26	45	GC Crew	


Project: Loft Project Schedule 6
Date: Fri 9/11/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	
47			Install ceiling clouds per finishes schedule	3 days	Mon 11/30/26	Wed 12/2/26		GC Crew	2
48			Install wall decoration per finishes schedule	3 days	Thu 12/3/26	Mon 12/7/26	47	GC Crew	
49			Install carpeting per finish schedule	2 days	Tue 12/8/26	Wed 12/9/26	48	GC Crew	
50			Install floor concrete finishing	2 days	Thu 12/10/26	Fri 12/11/26	49	GC Crew	
51			CLEAN UP	1 day	Mon 12/14/26	Mon 12/14/26			
52			Perform final clean up	1 day	Mon 12/14/26	Mon 12/14/26	50	GC Crew	
53			Substantial Completion Date	1 day	Mon 12/14/26	Mon 12/14/26	50		
54			CLOSE OUT	3 days	Tue 12/15/26	Thu 12/17/26			
55			Perform final inspection	2 days	Tue 12/15/26	Wed 12/16/26	53	Client PM,GC Manager	
56			Submit warranty documents	1 day	Thu 12/17/26	Thu 12/17/26	55	GC PM	

Project: Loft Project Schedule 6
Date: Fri 9/11/26



Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

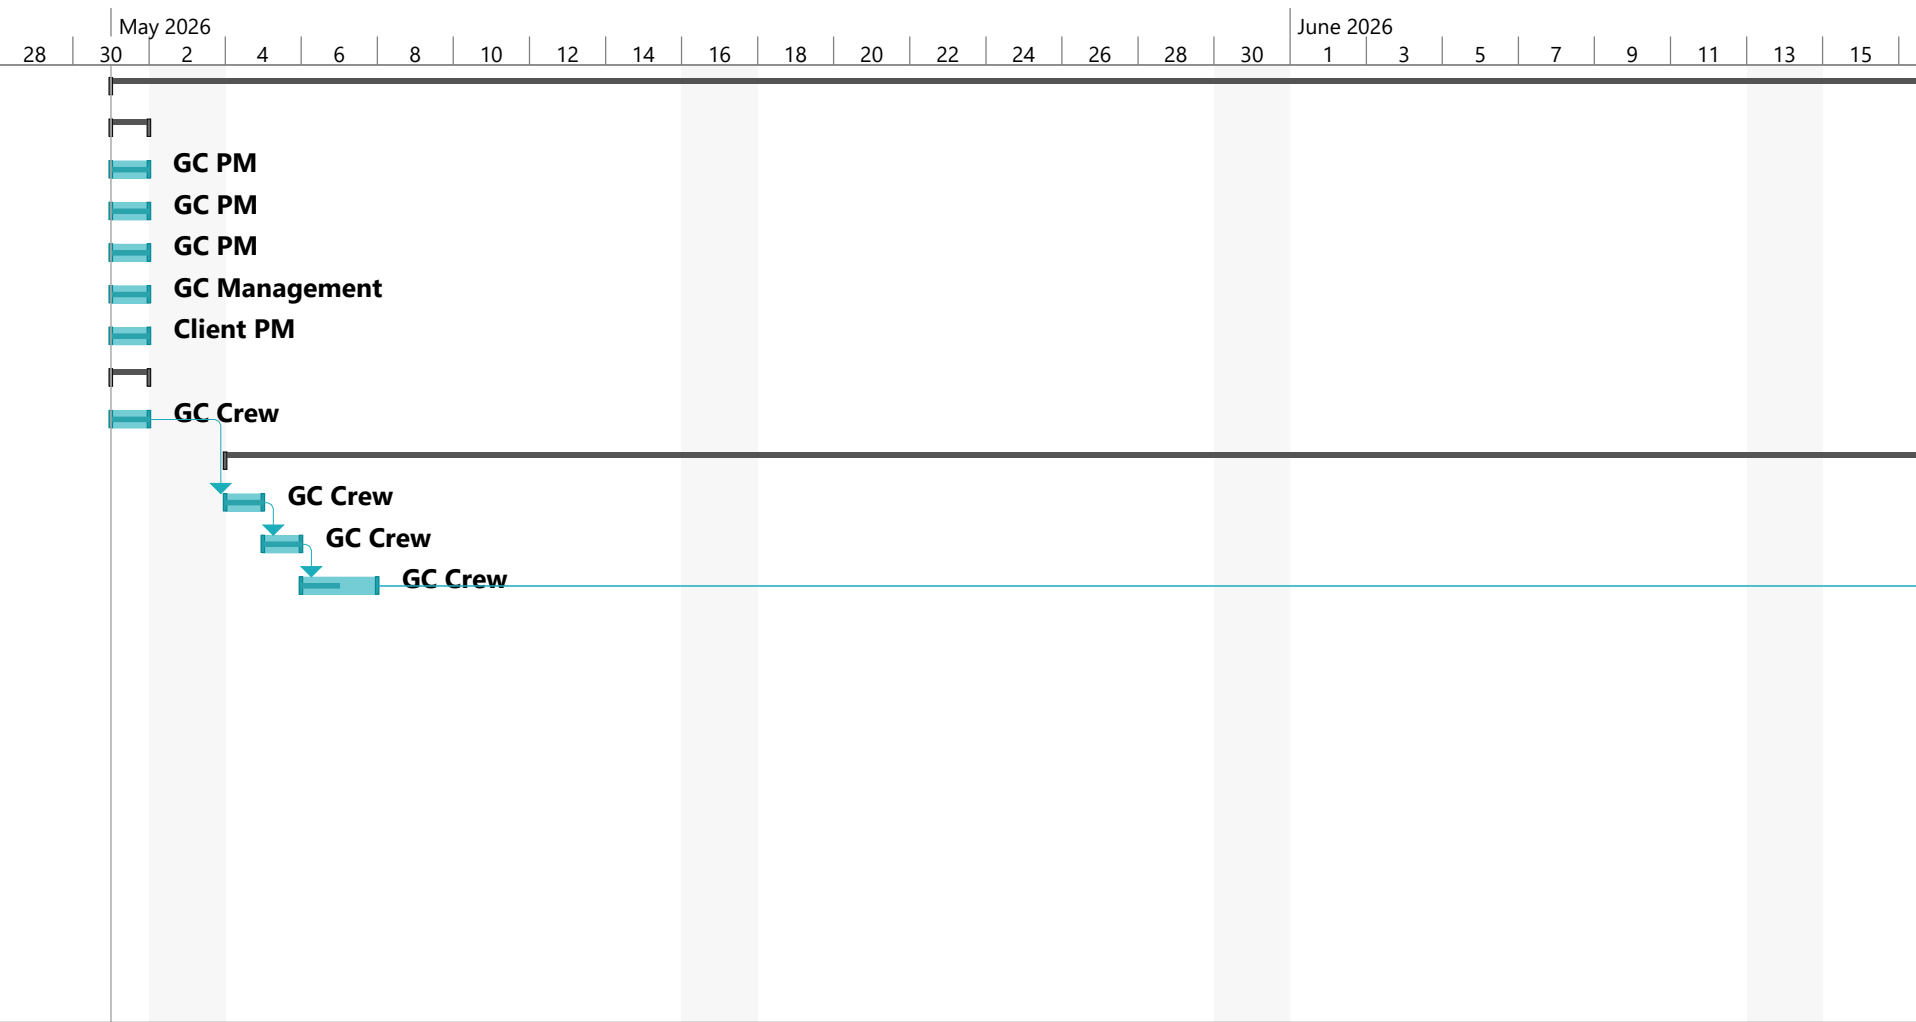


Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			






Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

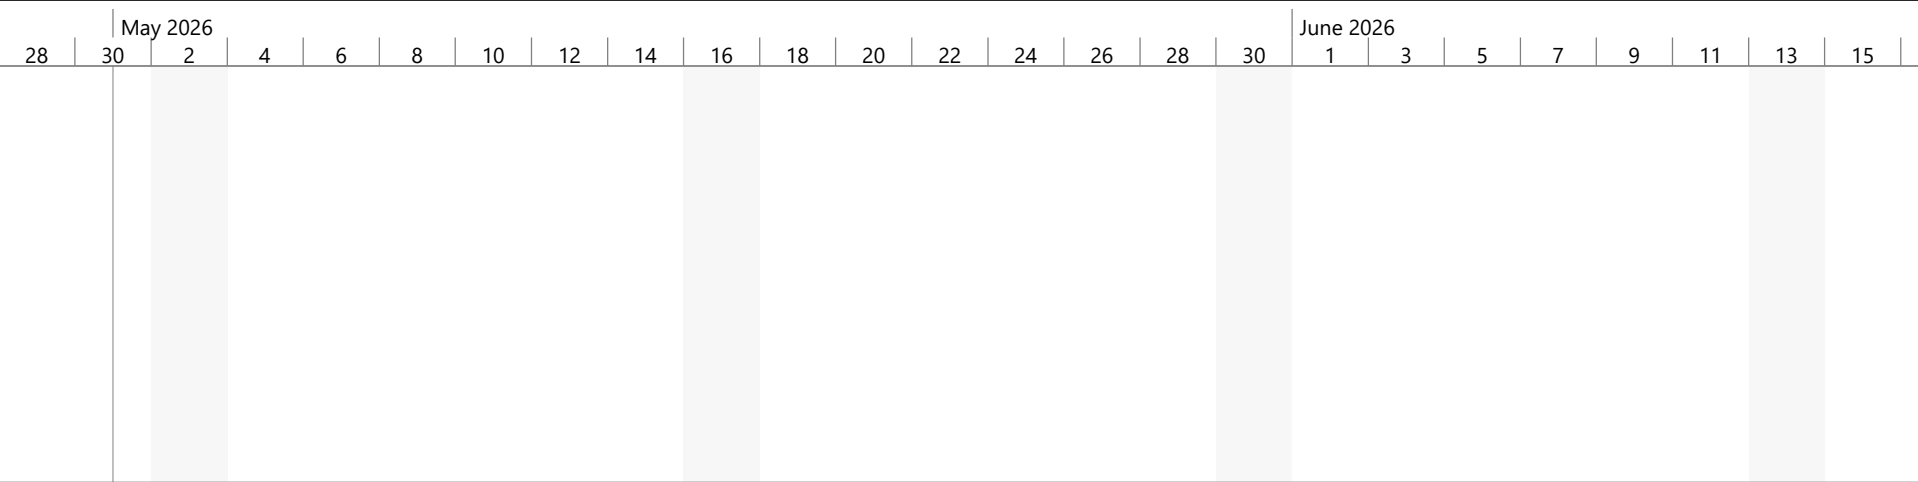


Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

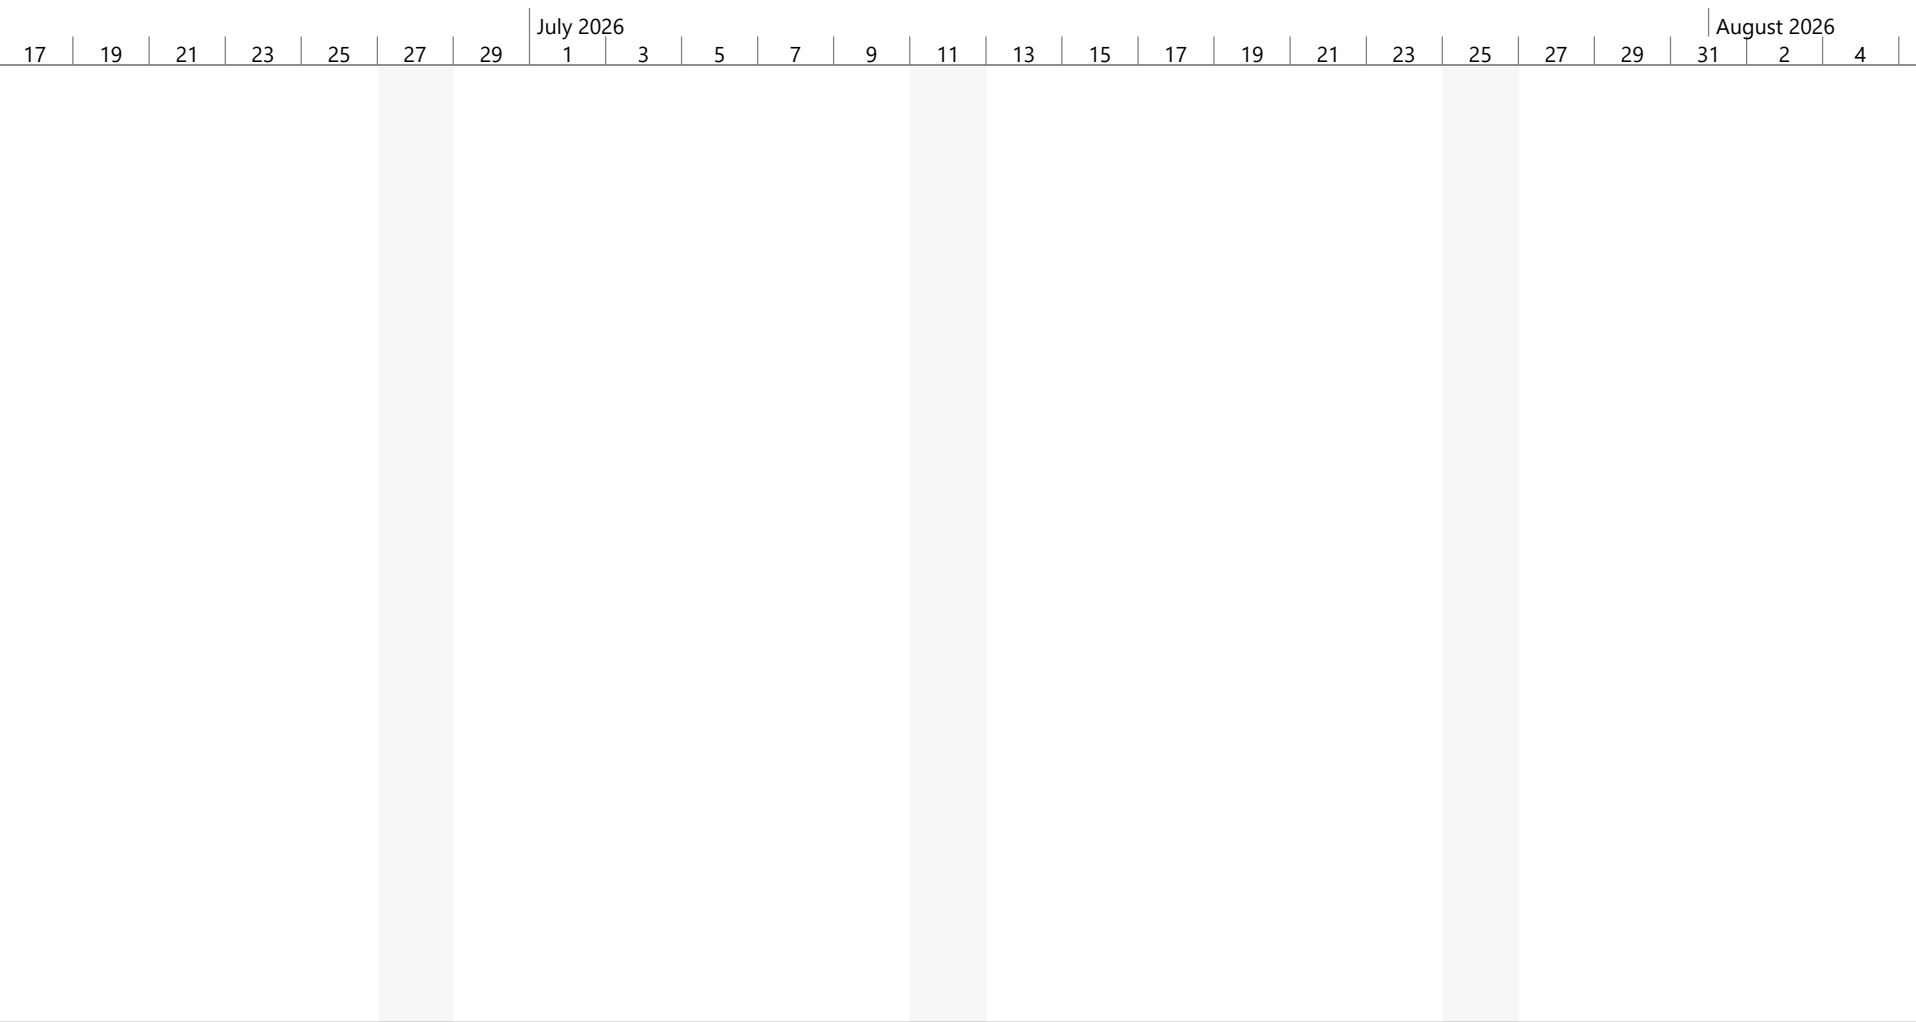

Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

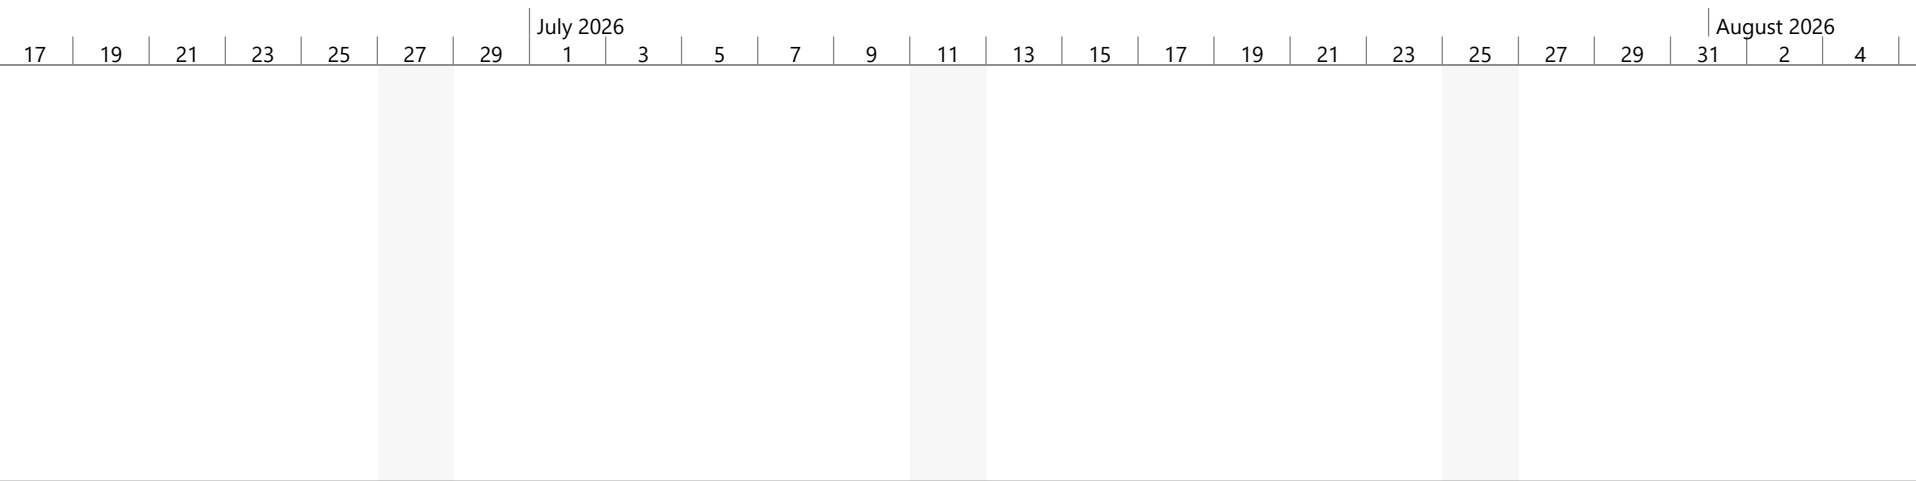


Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

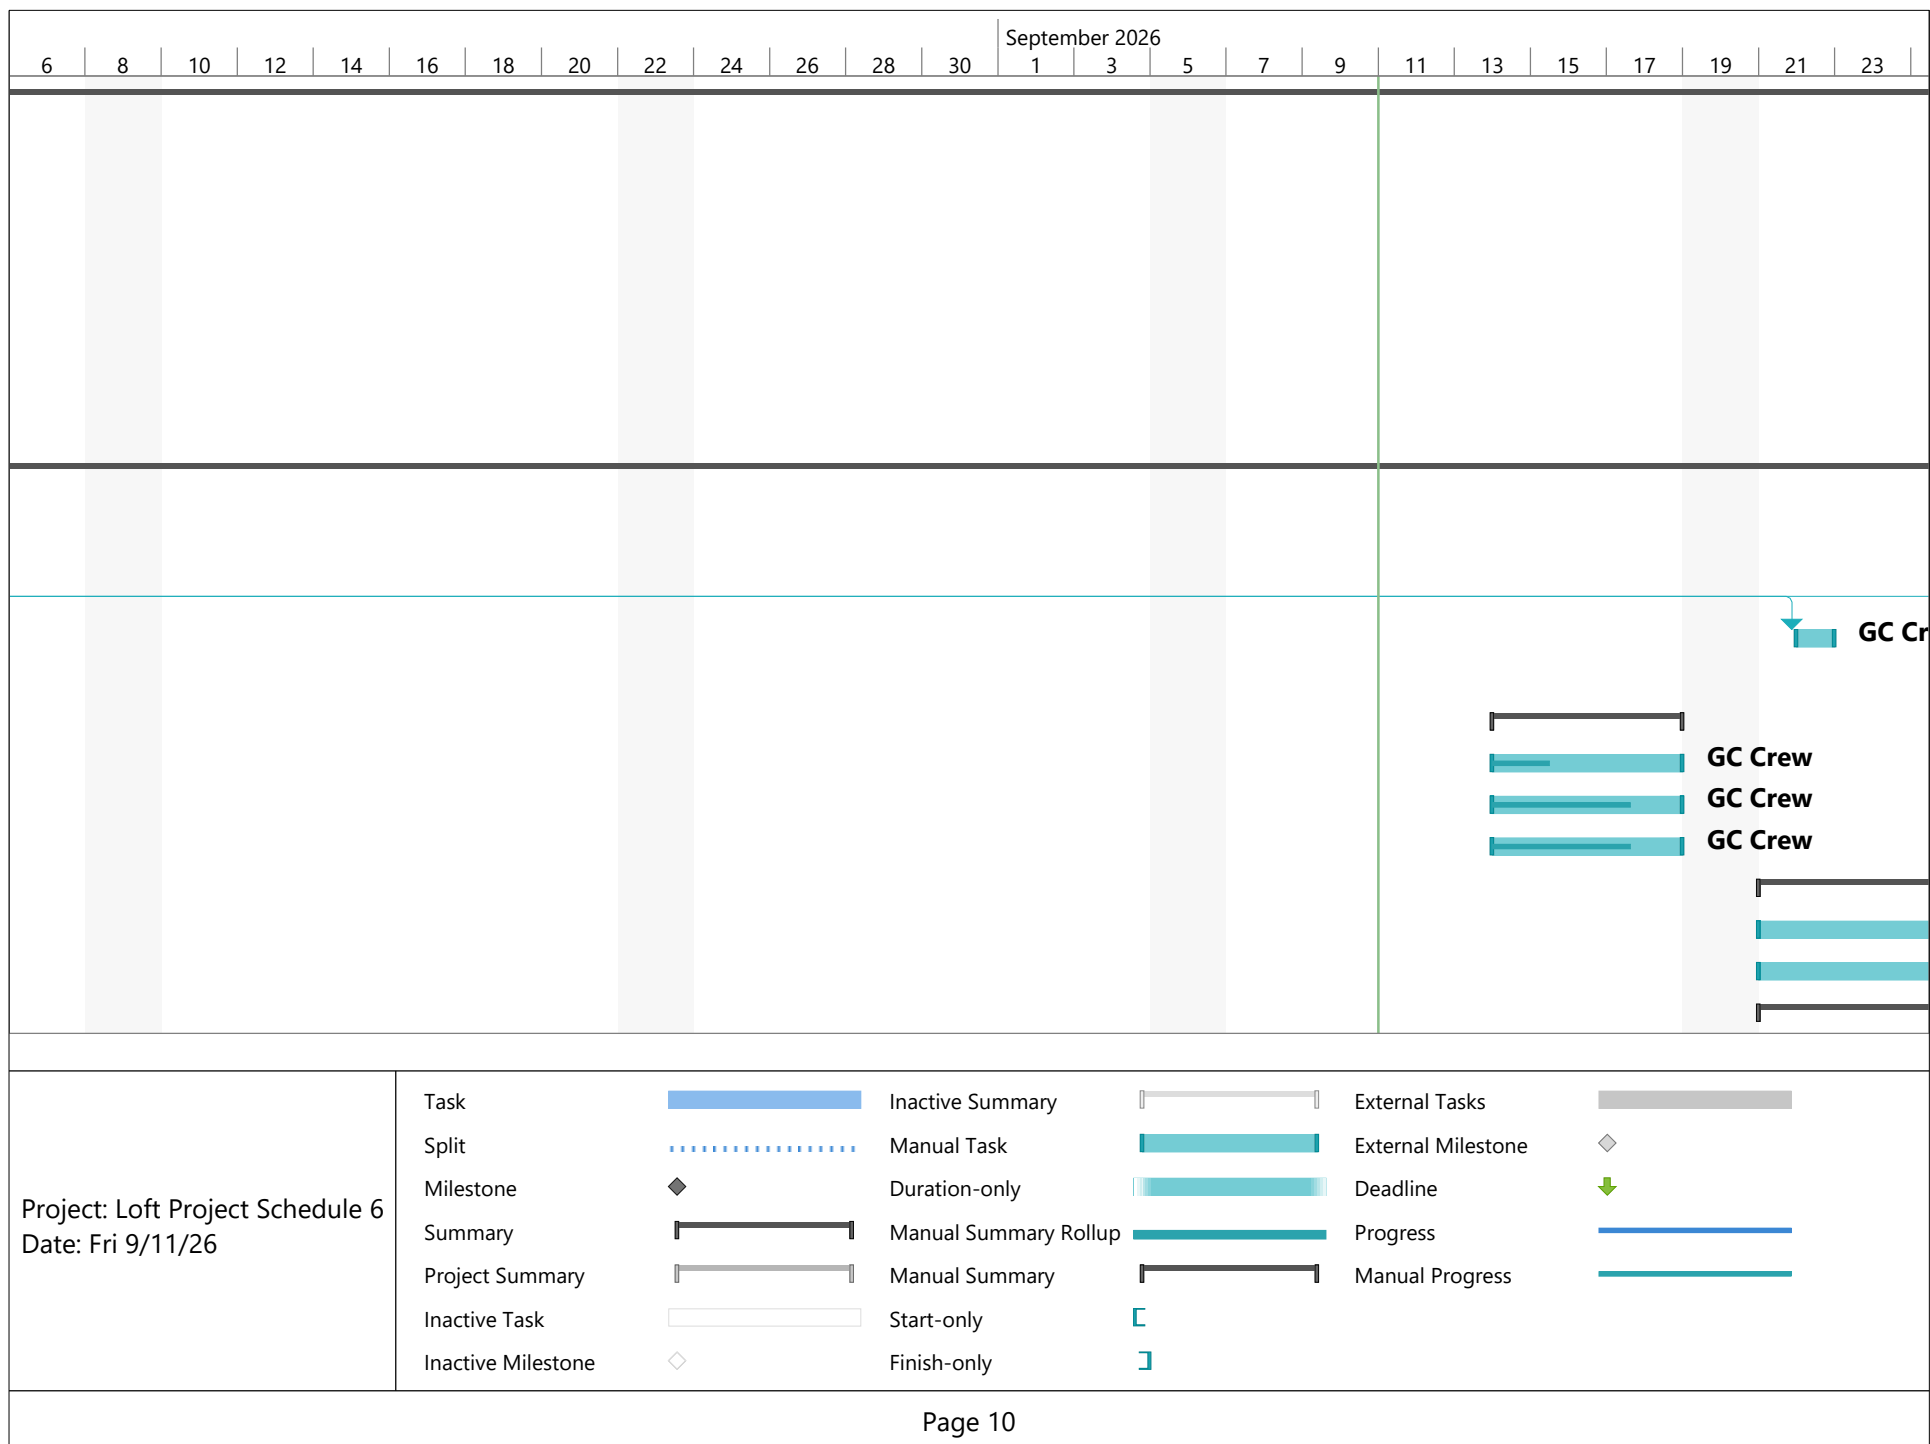




Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			





Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

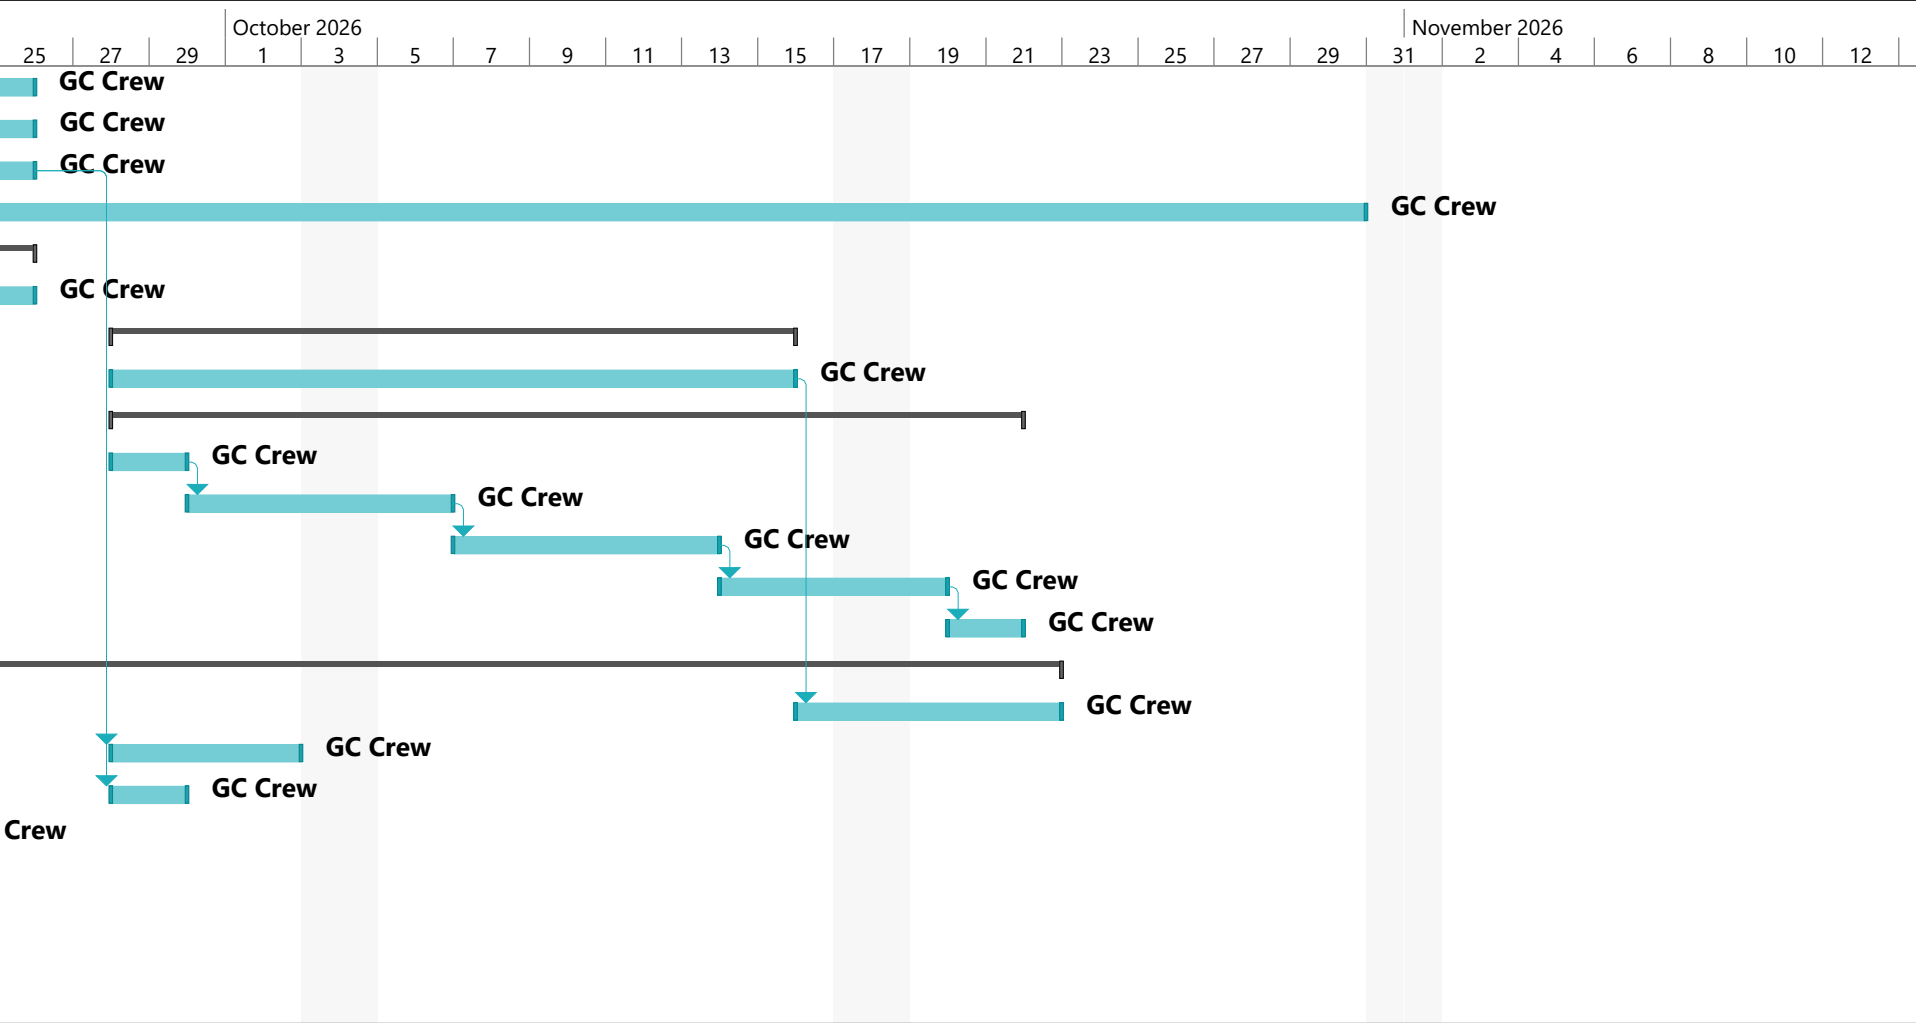


Project: Loft Project Schedule 6
Date: Fri 9/11/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

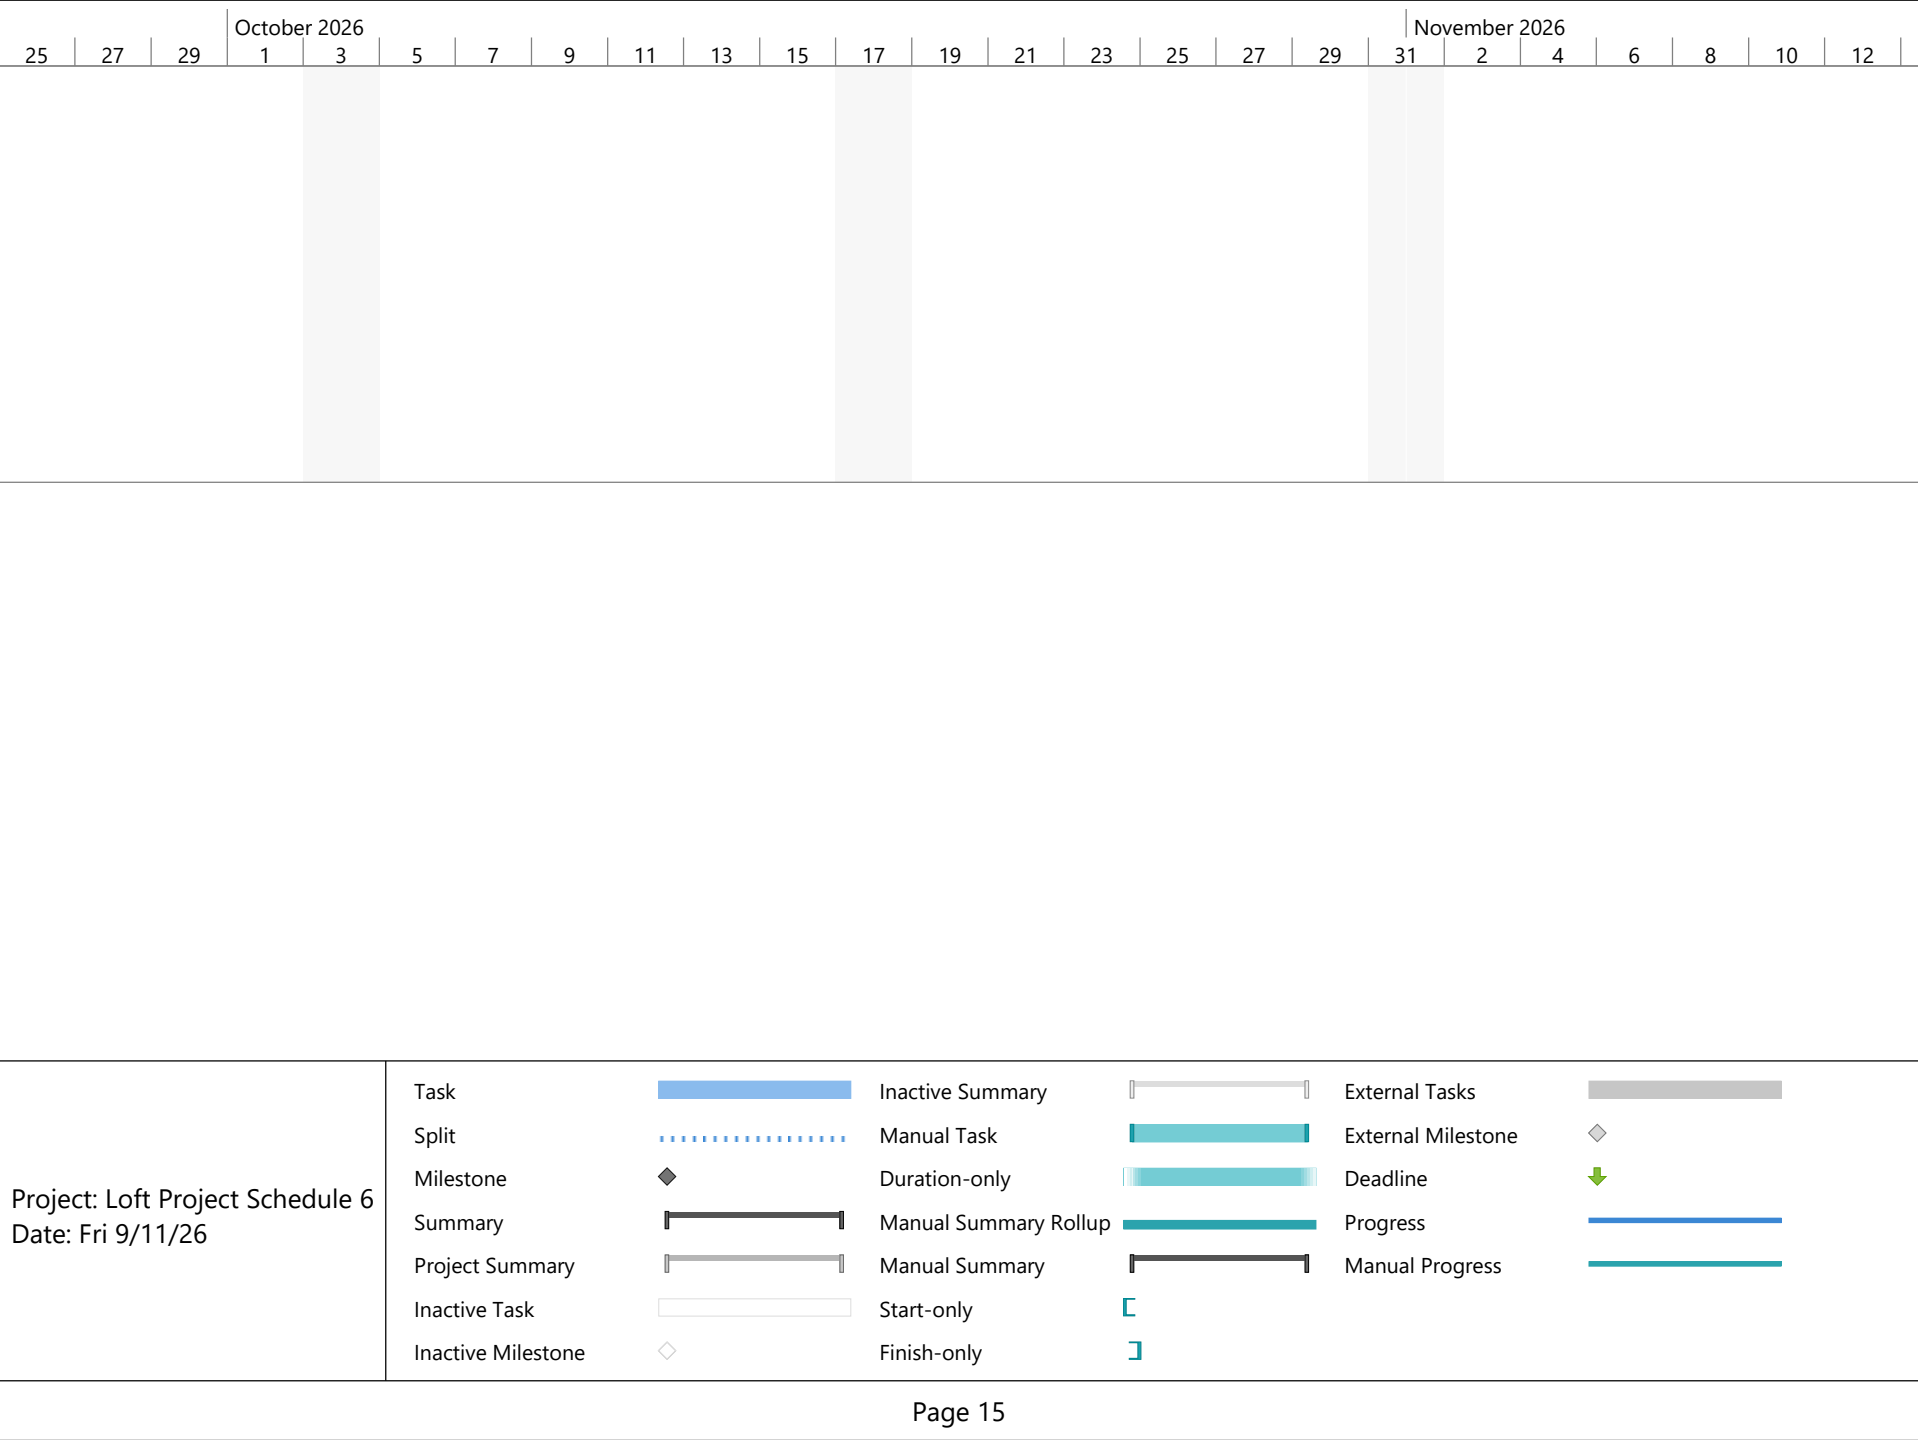

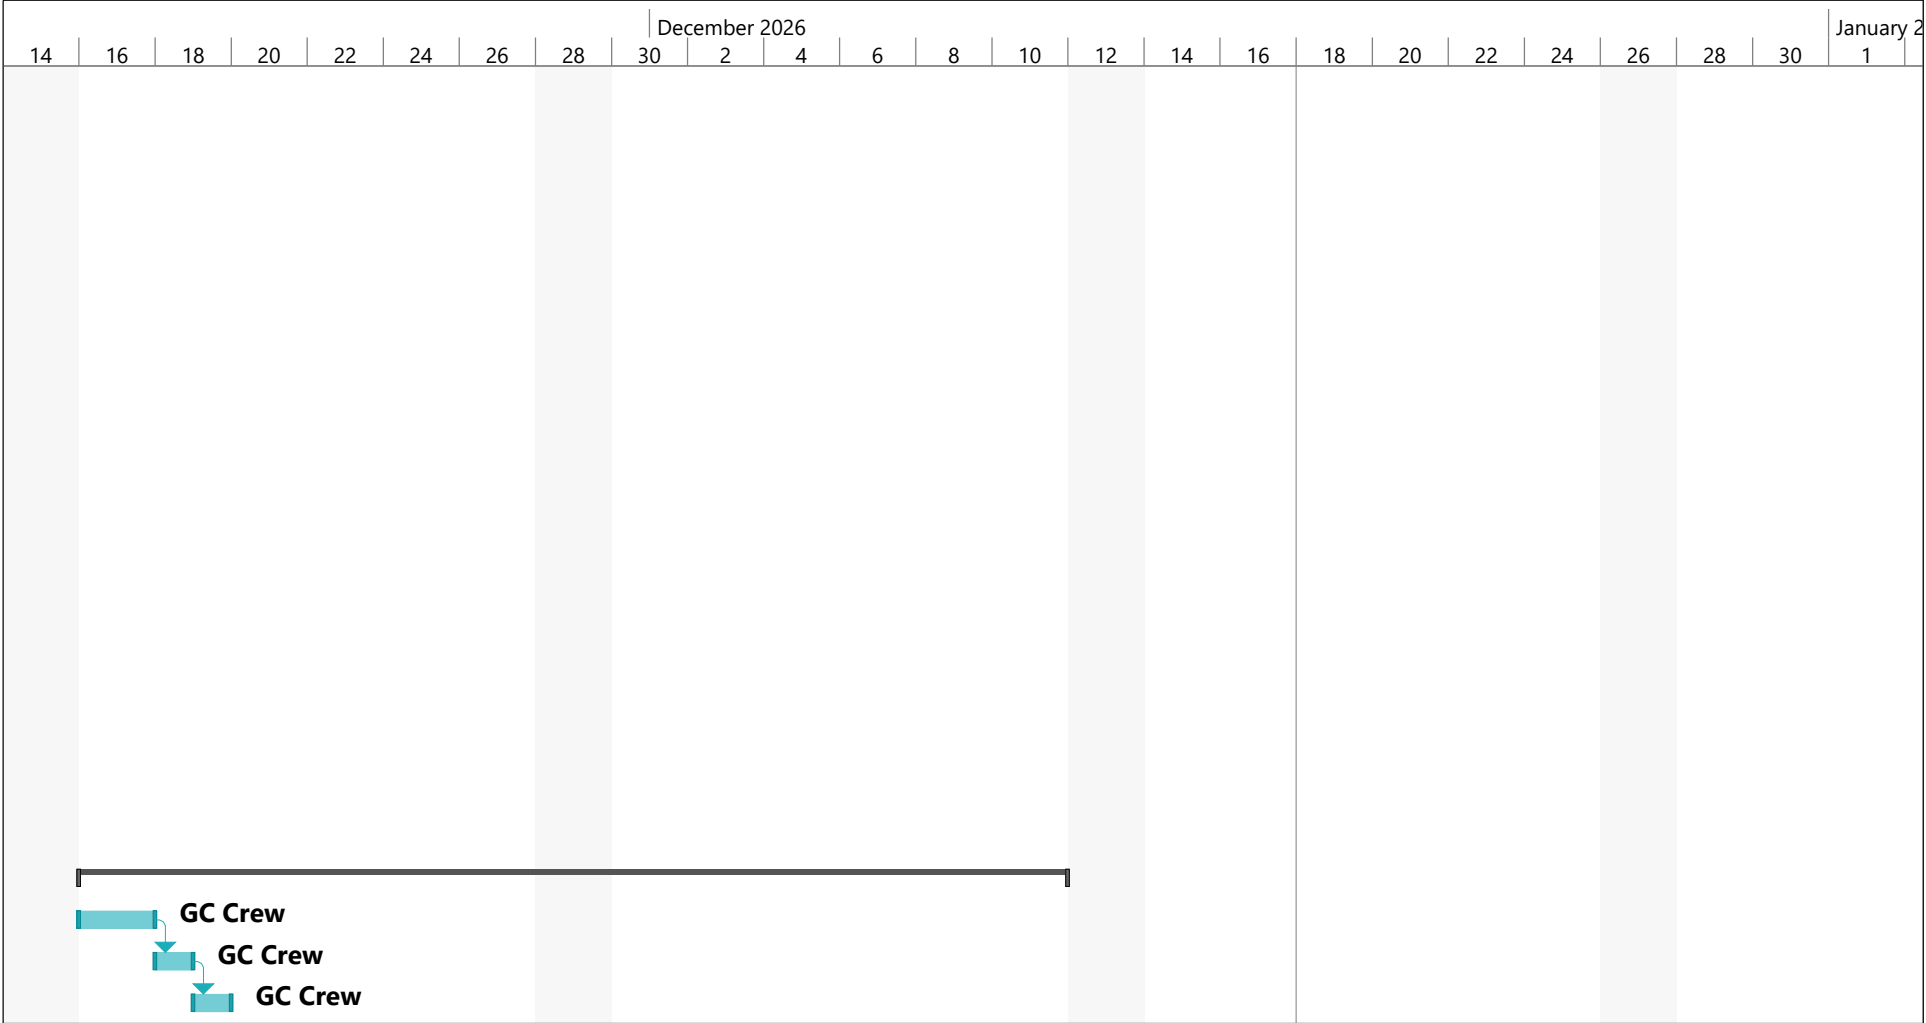

Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

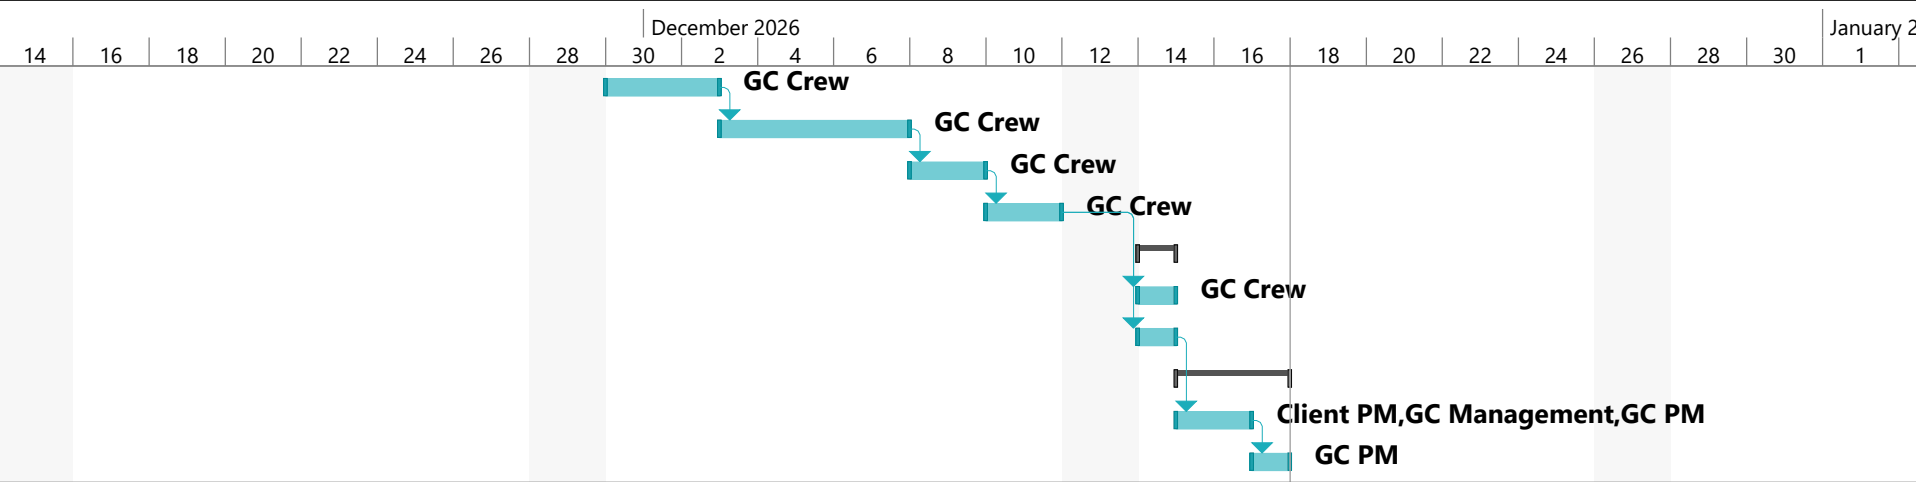

Project: Loft Project Schedule 6 Date: Fri 9/11/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
