SPOSETO ENGINEERING, INC.

4558 CONTRACTORS PLACE
LIVERMORE, CA 94551

Phone 925-443-4200 Fax 925-443-6800

SUBMITTAL NO: **003** DATE: 15-Mar-24 JOB NO: **S23745**

JOB NAME: **CITY OF EAST PALO ALTO**
SIGNAGE & BUS SHELTER IMPROVEMENTS PROJECT.
PUBLIC WORKS PROJECT NO. ST-25

DESCRIPTION: **CMP Schedule**

NOTE:
USE FOR :
SUPPLIER : **Sposeto Engineering**
SPEC. SECTION:

CREATED BY: Duy Truong DATE: 15-Mar-24

Activity ID	Activity Name	At Completion Duration	Start	Finish
S23745	**EAST PALO ALTO - BUS SHELTER IMPROVE**	427	15-Dec-22 A	27-Aug-24
S23745.1	**ADMINISTRATIVE**	427	15-Dec-22 A	27-Aug-24
A1000	ADMINISTRATION PERIOD	41	15-Dec-22 A	22-Feb-23 A
A1010	SUBMITTALS	7	22-Feb-24 A	01-Mar-24 A
A1030	NOTICE TO PROCEED	67	01-Mar-24 A	03-Jun-24 A
A1035	BUS SHELTER LEAD TIME	92	01-Mar-24 A	08-Jul-24 A
A1040	PROJECT COMPLETION	62	03-Jun-24*	27-Aug-24
S23745.2	**SITE CONSTRUCTION**	62	03-Jun-24	27-Aug-24
S23745.2.1	**BUS LOCATION 2, 6, 8**	10	03-Jun-24	14-Jun-24
A1540	TRAFFIC CONTROL	10	03-Jun-24*	14-Jun-24
A1550	SWPP	10	03-Jun-24	14-Jun-24
A1560	REMOVE BUS SHELTER / DEMOLITION	4	03-Jun-24*	06-Jun-24
A1570	EXCAVATION AND ROCK	3	07-Jun-24*	11-Jun-24
A1580	FORM AND POUR SIDEWALK / BUS STOP PAD	3	12-Jun-24*	14-Jun-24
S23745.2.2	**BUS LOCATION 3, 5**	10	17-Jun-24	28-Jun-24
A1725	TRAFFIC CONTROL	10	17-Jun-24*	28-Jun-24
A1735	SWPP	10	17-Jun-24	28-Jun-24
A1745	REMOVE BUS SHELTER / DEMOLITION	4	17-Jun-24*	20-Jun-24
A1755	EXCAVATION AND ROCK	3	21-Jun-24*	25-Jun-24
A1765	FORM AND POUR CURB RAMP / BUS STOP PAD	3	26-Jun-24*	28-Jun-24
A1835	INSTALL NEW TRUNCATED DOMES	3	26-Jun-24	28-Jun-24
S23745.2.3	**BUS LOCATION 1, 4, 7**	14	01-Jul-24	18-Jul-24
A1775	TRAFFIC CONTROL	14	01-Jul-24*	18-Jul-24
A1785	SWPP	14	01-Jul-24	18-Jul-24
A1795	REMOVE BUS SHELTER / DEMOLITION	4	01-Jul-24*	04-Jul-24
A1805	EXCAVATION AND ROCK	5	05-Jul-24*	11-Jul-24
A1815	FORM AND POUR SIDEWALK / DRIVEWAY / BUS STOP PAD	5	12-Jul-24*	18-Jul-24
S23745.2.4	**FINAL PHASE**	28	19-Jul-24	27-Aug-24
A1713	TRAFFIC CONTROL	28	19-Jul-24	27-Aug-24
A1714	SWPP	28	19-Jul-24	27-Aug-24
A1715	INSTALL BUS SHELTER	20	19-Jul-24*	15-Aug-24
A1825	INSTALL EURO BENCH / TRASH CAN /	5	19-Jul-24	25-Jul-24
A1845	PUNCH LIST	8	16-Aug-24*	27-Aug-24

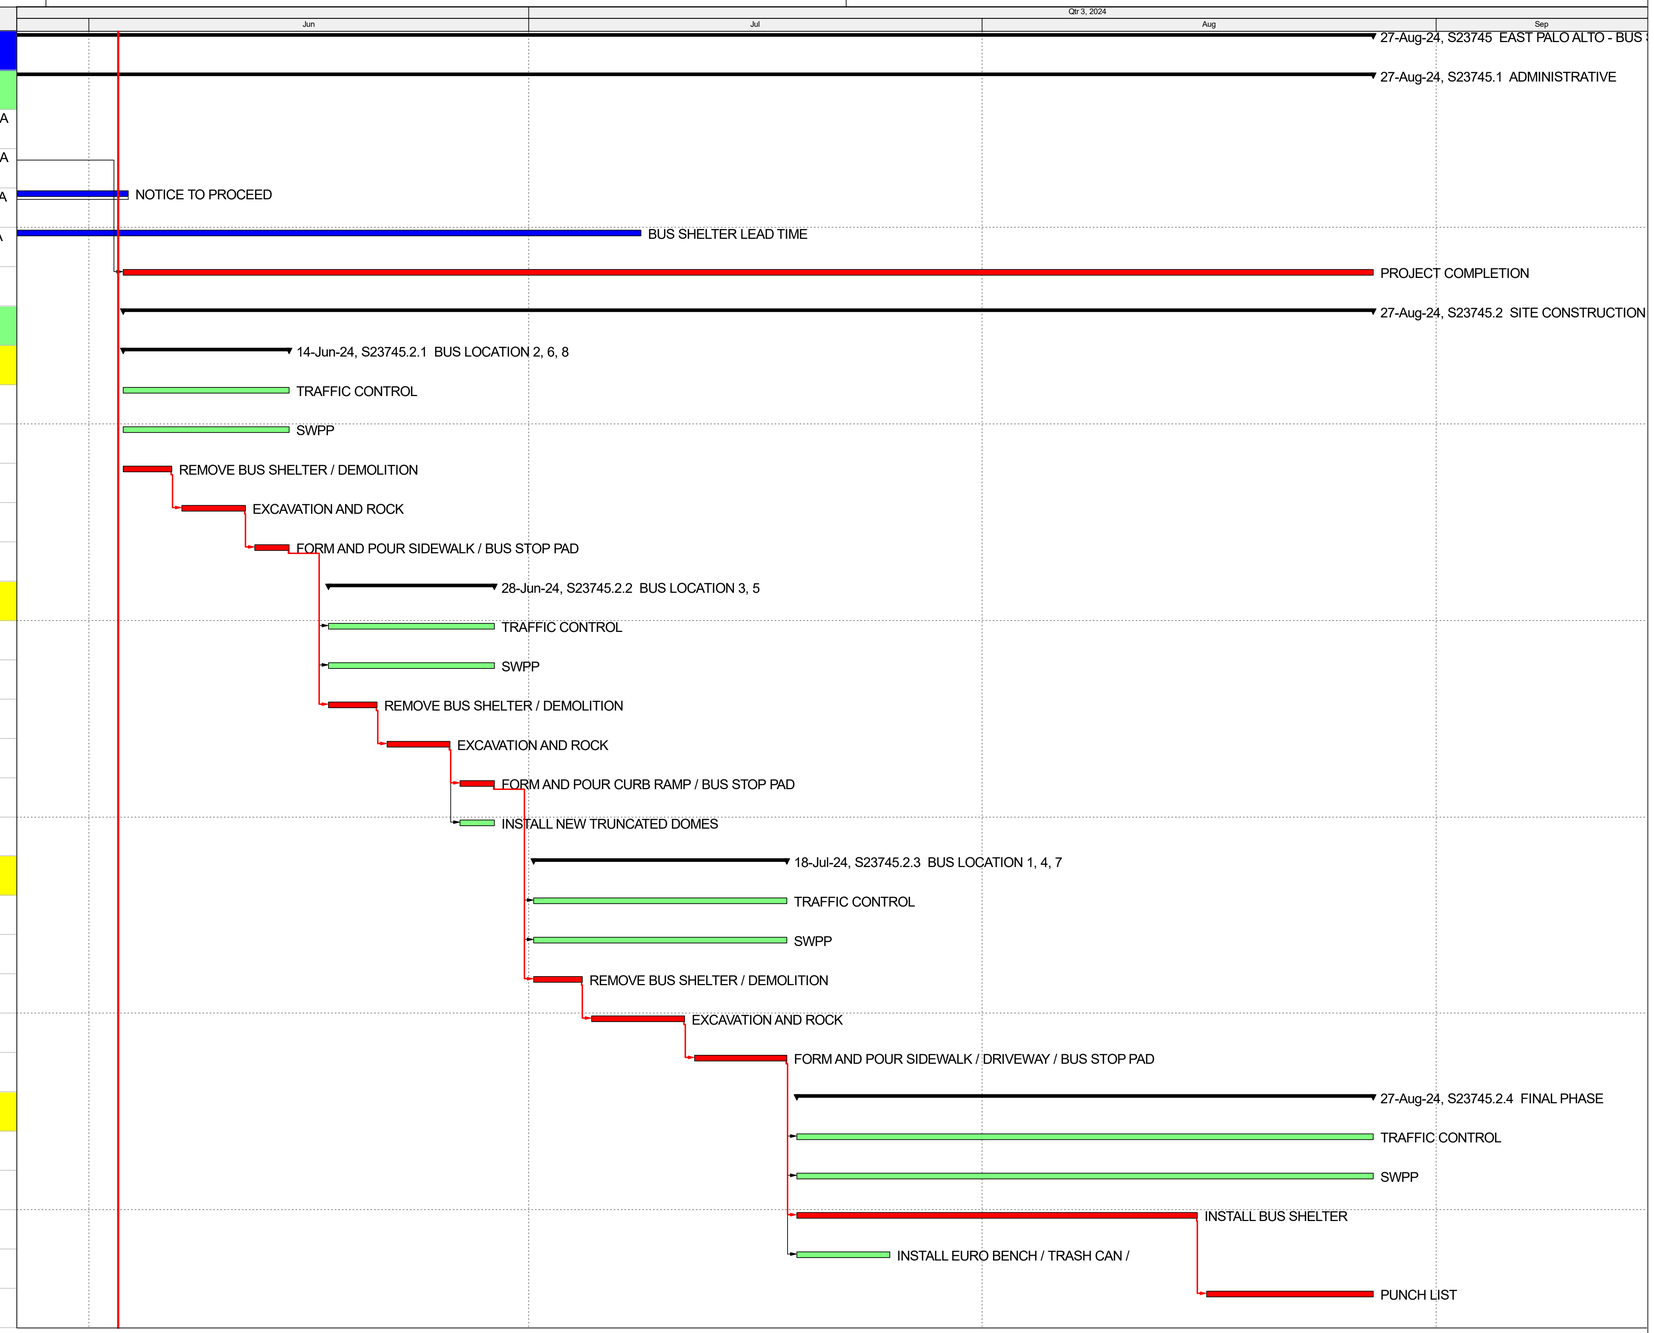

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
